



# HIGHWAY 25 SAFETY AND OPERATIONAL ENHANCEMENTS PROJECT Council of San Benito County Governments

Construction Management Report No. 05  
October, 2009



Construction Start Date: June 1, 2009  
Expected Completion Date: May 5, 2010  
Percent Completed to Date: 42%  
Time Elapsed on Project: 45%

Project Team:

Owner: Council of San Benito County Governments  
Design: URS  
Construction Management: MNS Engineers, Inc.  
General Contractor: Pavex Construction Division (Graniterock)  
Contract Oversight: Caltrans

Construction Activity during October consisted of the following:

- Grading at Shore Rd and Tri Cal Chemical Yard
- Placement of Class 2 Aggregate Base on Traveled way from Sta. 97+20 to Sta. 131+00 on Stage 1
- Placement of Class 2 Aggregate Base at Shore Rd and Tri Cal Chemical Yard
- Installing Drainage Systems on Stage 1
- Paving Stage 1 Traveled way from Sta. 97+20 to 131+00
- Paved Intersection Widening at Shore Rd and Tri Cal Chemical Yard
- Placing Class 3 Base on Access Roads on Stage 1.



• Drainage System at Hudner Ln.



Pavex Installing Drainage System at Tri Cal Chemical Yard crossing Hwy 25






Widening at Shore Rd.



Minor Concrete at Tri Cal Lined V Ditch



Widening at Tri Cal Chemical Yard

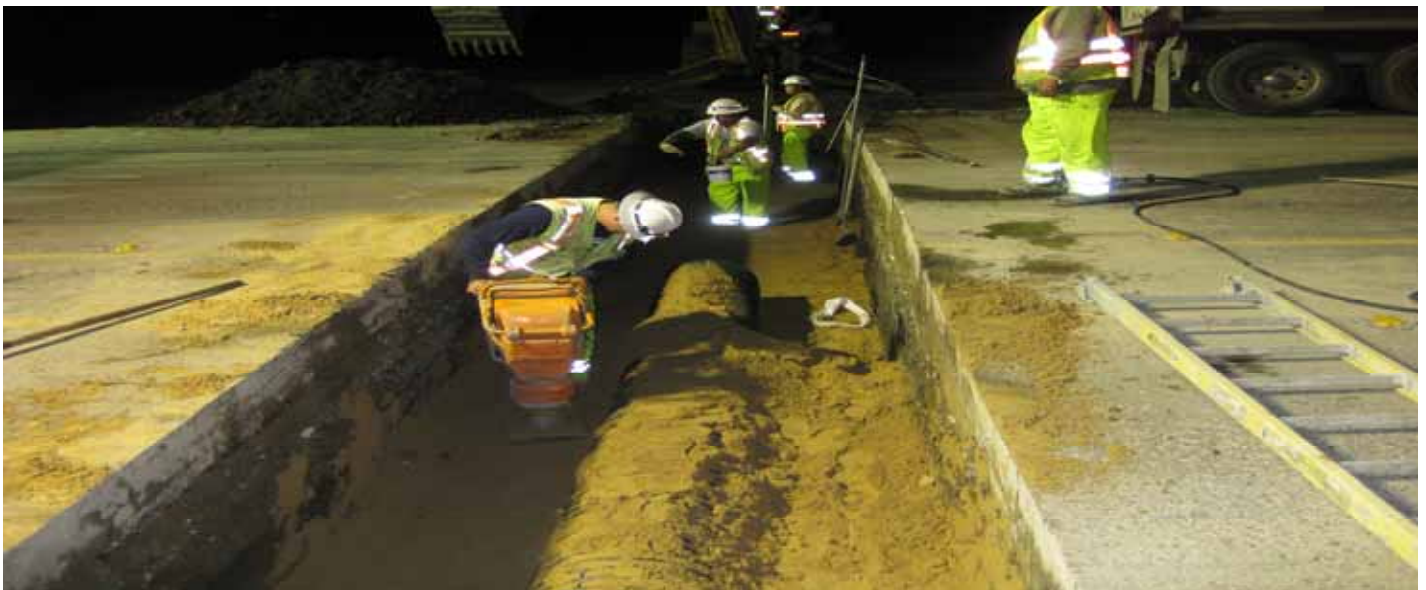

Pavex installing Drainage system at Tri Cal Chemical Yard



Construction Activity in November will consist of the following:

- Relocate Stage 1 Construction Barrier to Stage 2
- Installing Drainage systems on Stage 1
- Place Class 3 Aggregate on Access Roads
- Minor Concrete Work
- Placing Class 2 Base on Stage 2 Shoulder
- Paving on Stage 2 Shoulder
- Placing Stage 2 Temporary Stripe
- Placing Fence at Cattle Area Stage 1
- Build Headwalls for Drainage Systems in Stage 1
- Placing Fence on Stage 2
